



PROJECT SUMMARY REPORT

October 2018



AT A GLANCE

- Massive fill project with **62,000+ dump truck loads** of material being deposited into a **50-foot depression** near the terminal
- Resulting space will total more than **500,000 square feet** (more than **13 acres**)
- Added space will accommodate construction of BNA's new International Arrivals Facility (IAF)

- Project is being implemented in two phases:
 - **Phase 1:** Fill the depression and place asphalt. Completion: **Summer 2019**
 - **Phase 2:** Pave the space with concrete, which provides additional room for aircraft to park and maneuver when the IAF opens. Completion: **2023**

- Phase 1 design by **Garver**
- Phase 1 construction by **Eutaw Construction Company** and **Blakely Construction**

% Fill Deposited



550 Loads Deposited = 6,325 Cubic Yards (CY) 1% of Total Fill
1 LOAD = 11.5 CY
62,000 TOTAL LOADS = 632,500 CY

TOTAL PROJECT BUDGET

- Phase 1: \$26 million
- Phase 2: \$18 million (not yet awarded)
- Total: \$44 million

PROGRESS¹

- % of Fill Deposited, To Date: **62%**
- # of Dump Truck Loads of Fill Deposited, To Date: **38,440**
- Weight of Fill Deposited, To Date: **628,780 tons**
- # of Loads Deposited Per Day, To Date: **500**

SMWBE PARTICIPATION²

	GOAL	ACHIEVED	PROJECTED
WBE	11.48%	9.84%	11.48%

Construction


	GOAL	ACHIEVED	PROJECTED
DBE	7.00%	1.69%	7.00%
MBE/WBE	6.01%	0.00%	6.01%

WORK FORCE³

- Total # of Workers: **58**
- Regional Labor: **40%**
- Total Hours Worked: **42,000**

WORK FORCE BY COUNTY

- OTHER
- DAVIDSON
- WILLIAMSON
- RUTHERFORD
- LAWRENCE
- ROBERTSON
- SUMNER

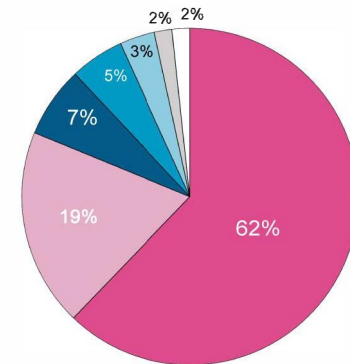

MATERIALS⁴

- % Regional Materials Used: **100%**
- Sources of Fill:
 - MNAA Stockpile, Extracted On-Site at BNA
 - External Sources

¹As of 10/4/2018 ²As of 8/31/2018 ³As of 10/4/2018 ⁴As of 10/4/2018
